
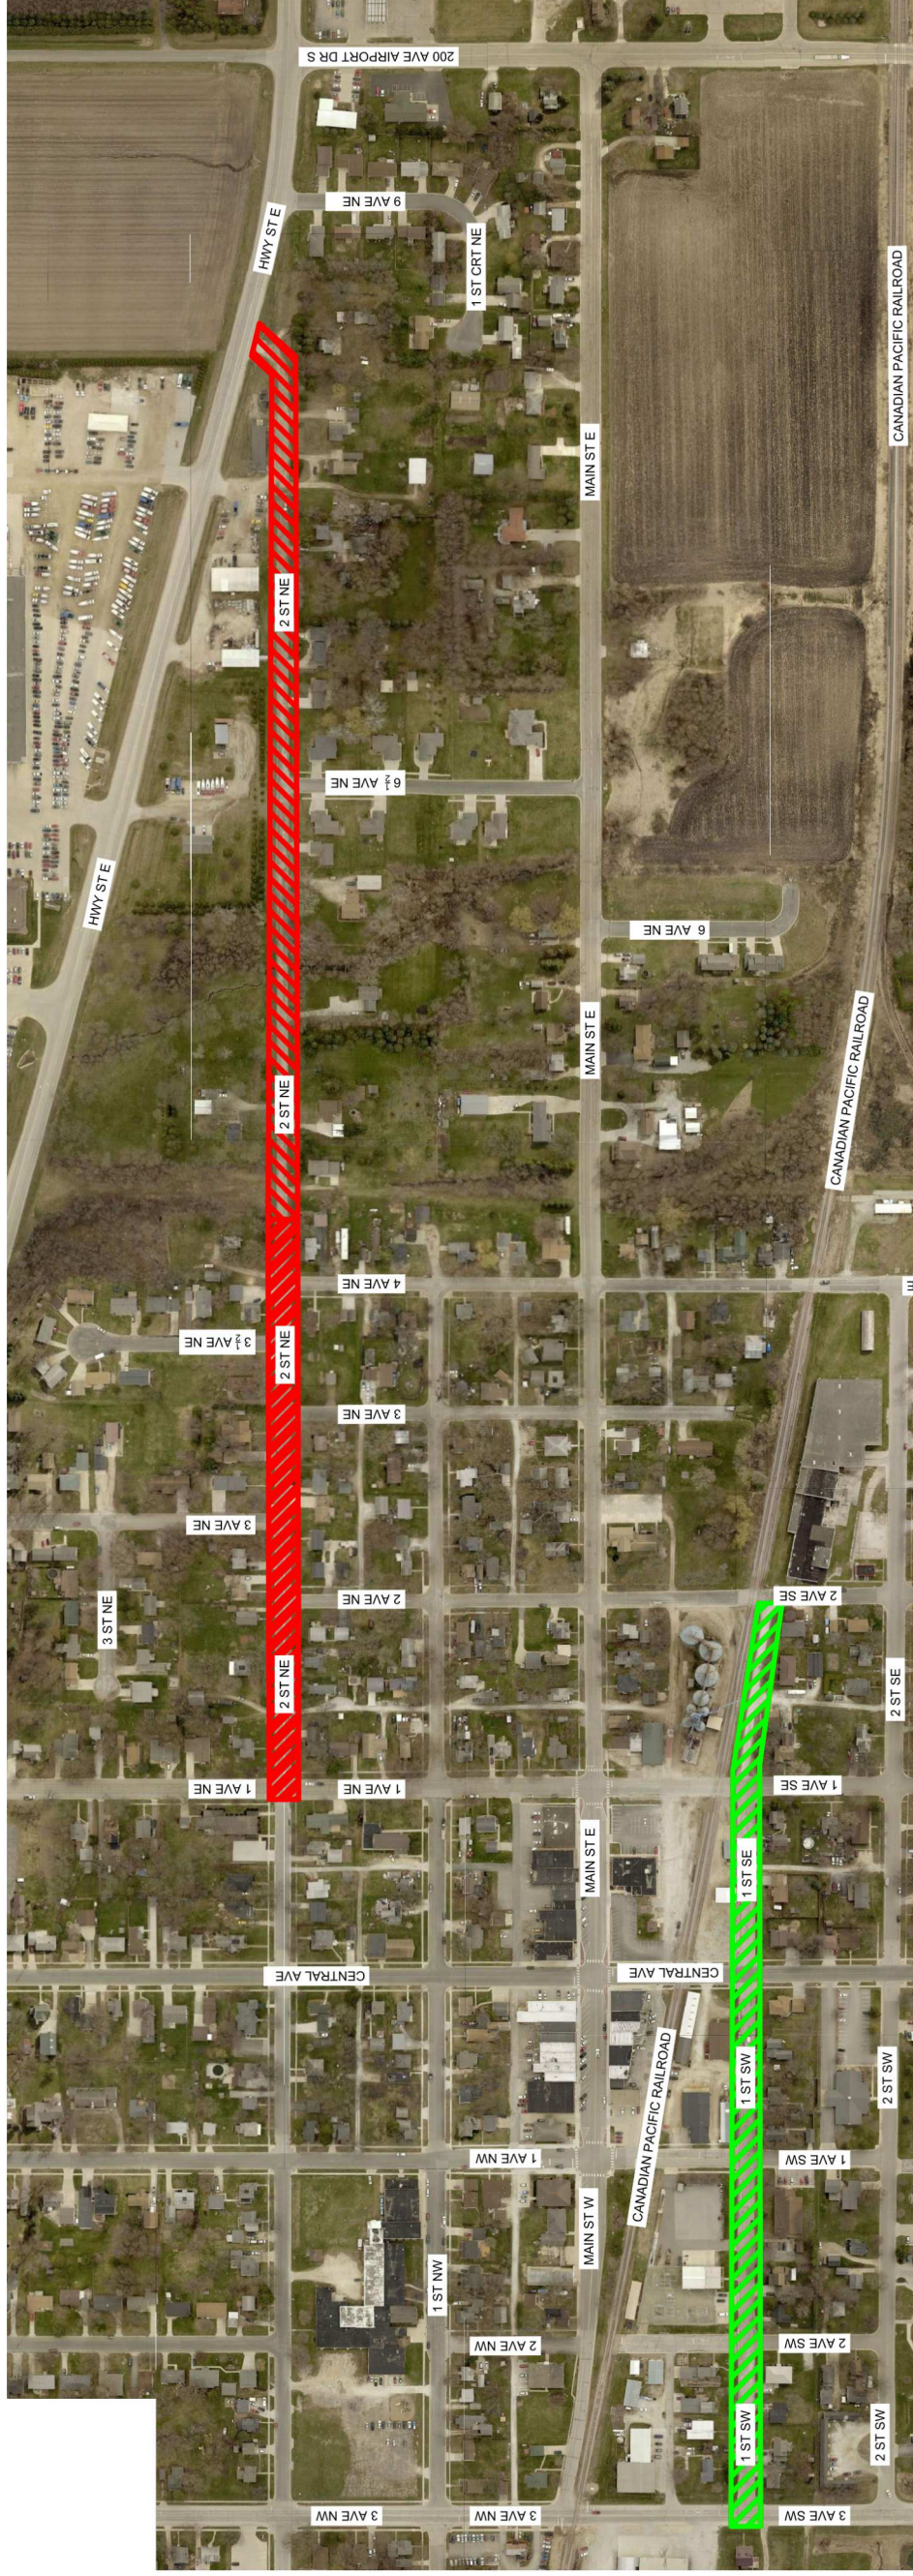


2020 STREET IMPROVEMENT PROJECT



2020 STREET IMPROVEMENT PROJECT

CURRENT CONSTRUCTION AREA: 1ST ST SW & SE & 2ND ST NE

1ST ST SW & SE

1. THE STREET IS BEING SUBCUT SO THE INTERSECTIONS WITH THE CROSS STREETS ARE TEMPORARILY CLOSED.
2. STREET CONSTRUCTION WILL CONTINUE FOR THE NEXT COUPLE OF WEEKS, CURB AND GUTTER IS PLANNED BE PLACED NEXT WEEK, WITH CONCRETE DRIVEWAYS TO FOLLOW LATER IN THE MONTH. TEMPORARY WATER SERVICE IS PLANNED TO BE REMOVED THIS WEEK.

2ND ST NE

3. THE REMOVAL OF TREES HAS STARTED AND WILL CONTINUE OVER

THE NEXT MONTH.

4. REMOVALS ON 2nd STREET NE HAS STARTED FROM 1st AVENUE NE TO 4TH AVENUE NE.
5. TEMPORARY WATER SERVICE TO BE INSTALLED ON 2nd STREET NE UP TO 4th AVENUE NE AND INCLUDING 3 1/2 AVENUE NE.
6. ONCE THE SANITARY SEWER IS INSTALLED TO 4th AVENUE NE, THE CONTRACTOR WILL BEGIN WATER MAIN INSTALLATION FROM 1st AVENUE NE TO 4th AVENUE NE.
7. THE CONTRACTOR IS TENTATIVELY SCHEDULED TO START THE 1st AVENUE NE INTERSECTION WORK ON FRIDAY. WHEN THE WORK DOES START ON THE SANITARY SEWER AND WATERMAIN IN THE INTERSECTION, THE INTERSECTION WILL BE CLOSED FOR TWO TO THREE DAYS.
